the BIG. Water Story Upplates

Programme Overview

May and June 2019, has seen the physical commencement of two further projects, we continue to progress a number of projects from tender to commencement. We expect the next two-three months will continue this trend and up to nine Big Water Story projects may be underway across the district.

You can find out more detail on #thebigwaterstory projects by visiting our website www.chbdc.govt.nz

As part of Project Thrive, the importance of water to our community came through loud and clear!

Through the #thebigwaterstory we are bringing Project Thrive Alive.


Key Projects Focus

Find out more below about some key projects currently happening in our community.




Central Hawke's Bay Wastewater Improvements

June 2019 saw the culmination of a years' worth of work to prepare a response to the environment court in relation to a breach of resource consent conditions. The project now shifts to the next phase where the team will focus on continuing to improve the performance of the plants, developing a consenting strategy, progressing funding and financing work streams in preparation to take options to the community for a long term solution.



Waipukurau Firefighting

From approximately Monday 29th July 2019 works are planned to commence on this project to improve firefighting capacity, shortfalls in supply and resilience of the Waipukurau water network. This project will see the first 2 of a 7 stage upgrade to the water network to better address security of supply, resolve areas of fire flow compliance, and allow for future connections within the urban boundary to service future growth.

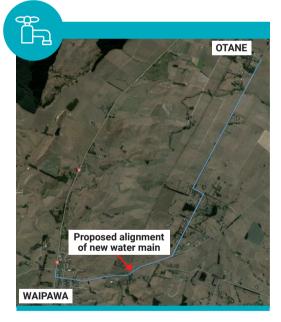

Otane Alternate Water Supply

Works are expected to commence on-site the week of the 15th July 2019 on one of our largest projects within #thebigwaterstory through to expected completion in December 2019.

The construction will see a 180mm polyethylene (PE) pipeline laid from the existing Waipawa water supply on SH2, running along Racecourse Road, crossing the railway on Racecourse Road and running into and along White Road, finally connecting into new supply on the corner of Knorp and White Road. This exciting 5.2km new pipeline project will see significant resilience and security of water supply added to the Otane network.

PROJE

Otane Alt

Waipuku

Waipuku

Waipuku

Otane La

Waipuku

Porangah

Takapau

Waipuku

PROJE

Waipuku Waipuku

Savage/0

Waipuku

Waipuku

PROJE

Waipawa

CHB Was

CHB Was

CHB Was

Otane Wa

Otane W

Otane to

Takapau

Takapau

Porangał

CHB Floa

July 2019



Individual Project Updates

	WATER			
ECT	STATUS	TIMELINE	PROGRESS	BUDGET (TOTAL)
Alternate Water Supply	Build	<i>Start:</i> Aug 2018 <i>End:</i> June 2020	20%	\$2.6m
xurau Second Water Supply	Design	<i>Start:</i> Aug 2018 <i>End:</i> June 2021	10% ••••••	\$5.6m
kurau SH2 Bore Upgrade	Contract Negotiations	<i>Start:</i> June 2018 <i>End:</i> Dec 2019	20%	\$850k
xurau Firefighting and Shortfalls Improvements (Year 1-3)	Build	Start: Aug 2018 End: June 2021	20%	\$1.47m
Land Development (Water and Wastewater)	Complete	Start: March 2018 End: Dec 2018	100%	\$355k
kurau – Porritt Place Water Main Renewal	Complete	Start: Dec 2018 End: March 2019	100%	\$65k
ahau Water Treatment Plant Upgrade	Build	<i>Start:</i> Nov 2018 <i>End:</i> Oct 2019	30%	\$1.03m
u Water Treatment Plant Upgrade	Build	<i>Start:</i> Nov 2018 <i>End:</i> Oct 2019	30%	\$680k
kurau – Mackie/Mclean St Water Main Renewal	Build	<i>Start:</i> Nov 2018 <i>End:</i> Aug 2019	80%	\$391k
STORMWATER				
ECT	STATUS	TIMELINE	PROGRESS	BUDGET (TOTAL)
xurau Stormwater Improvements – Service Lane Overflow	Design	<i>Start:</i> Aug 2018 <i>End:</i> Dec 2019	20%	\$132k
kurau Stormwater Improvements – e/Churchill/Carpenter – Woburn/Wilder	Build	<i>Start:</i> Aug 2018 <i>End:</i> Dec 2019	20%	\$481k
xurau Stormwater Helicoil Upgrades – Jellicoe to Tavistock	Build	<i>Start:</i> Aug 2018 <i>End:</i> Aug 2019	40% ●●○○○	\$219k
kurau Stormwater Helicoil Upgrades – Francis Drake Street	Build	Start: Aug 2018 End: Aug 2019	70% ●●●●○○	\$280k
	ASTEWATER			
ECT	STATUS	TIMELINE	PROGRESS	BUDGET (TOTAL)
va Trunk Sewer Main Renewal	Engagement & Build	Start: Aug 2018 End: June 2020	20%	\$1.77m
astewater Treatment Plants Project (Phase 1)	Engagement & Court Report	Start: June 2018 End: June 2019	90%	\$300k
astewater Treatment Plants Project (Phase 2 – Design & Consent)	Investigation	Start: July 2019 End: Dec 2020	5% 00000	\$1.8m
astewater Treatment Plants Project (Phase 3 – Build)	Not Started	Start: Jan 2021 End: TBC	0% 00000	TBC
Wastewater Infiltration and Inflow Study	Build	Start: Jan 2019 End: June 2019	30%	\$80k
Wastewater Treatment Plant Upgrade	Investigation	Start: April 2018 End: March 2021	40%	\$1.47m
to Waipawa Wastewater Pipeline	Design	Start: June 2019 End: March 2021	5% 00000	TBC
u Wastewater Resource Consent Extension	Part 1 – Complete	Start: Aug 2018 End: June 2021	50%	\$100k
u Wastewater Treatment Plant Upgrade	Not Started	Start: 2019 End: 2022	0% 00000	\$831k
ahau/Te-Paerahi Wastewater Treatment Plant Upgrade	Not Started	Start: 2019 End: 2022	0% 00000	\$1.85m
oating Wetlands Review	Investigations	Start: April 2019 End: TBC	5% 00000	TBC

CENTRAL HAWKE'S BAY DISTRICT COUNCIL

www.chbdc.govt.nz • thebigwaterstory@chbdc.govt.nz • 06 857 8060 PO Box 127 • 28 - 32 Ruataniwha Street, Waipawa 4210 Together we Thrive! E ora ngātahi ana!

